## INFORMATIONAL MEMORANDUM

TO: Transportation and Infrastructure Services Committee
FROM: Hari Ponnekanti, Public Works Director/City Engineer

BY: Deontae Elder, Transportation Project Manager

CC: Mayor Ekberg
DATE: June 17, 2022

SUBJECT: 2022 Overlay and Repair Program

Project No. 80010401

**Bid Award** 

#### **ISSUE**

Award the bid for construction of the 2022 Overlay and Repair Program.

#### **BACKGROUND**

The Overlay and Repair Program preserves and maintains the street structure in a safe and useable condition. Construction will include, but not be limited to pavement repairs, sidewalk improvements, signal improvements, and an asphalt overlay at seven locations citywide. Multiple projects were combined for the 2022 Overlay & Repair Program due to economy of scale, including work related to Overlay & Repair, Small Drainage, ADA improvements, and the Neighborhood Traffic Calming Program (NTCP).

#### **ANALYSIS**

A call for bids was advertised for the 2022 Overlay and Repair Program on May 11, 2022 and May 18, 2022. Four bids were opened on June 7, 2022. The bid was separated into two schedules, with Schedule B being an optional additive alternate if budget allowed. The confirmed lowest bidder was Tucci & Sons, with a bid of \$1,422,751.25 for Schedule A and \$189,858.50 for Schedule B. The Engineer's Estimate was \$1,438,725.00 for Schedule A and \$239,257.50 for Schedule B. There were no bidding errors.

Schedule A includes work at the following locations:

- 44<sup>th</sup> Ave S and 46<sup>th</sup> Ave S along S 124<sup>th</sup> St.: Work includes RRFB (Rectangular Rapid Flashing Beacons) installation, installation of curb ramps and sidewalk, driveway improvements, and channelization installation. This project is on the NTCP Top-10 priority list.
- **S 140**<sup>th</sup> **St. from Military Road to Tukwila International Boulevard:** Work includes grind and overlay, sidewalk and curb ramps installation, channelization such as stop bars, crosswalk, and paint lines, speed cushions, signs, driveways improvements, pavement repair, and gravel.
- Orillia Rd. and S 200<sup>th</sup> St. Intersection: Work includes pavement repair, grind and overlay, curb ramps, channelization, signal modifications such as traffic cameras, cabinets, loop removal, and pedestrian signal improvements, and driveway improvements.
- **S 141**st **St. from 37**th **to Tukwila International Blvd.:** Work includes grind and overlay, pavement repair, installing gravel, driveway improvements, and channelization installation.
- **S 142**<sup>nd</sup> **St. from 37**<sup>th</sup> **to Tukwila International Blvd.:** Work includes grind and overlay, pavement repair, installing gravel, driveway improvements, and channelization installation.
- 37<sup>th</sup> Ave S between S 144th St. and S 140<sup>th</sup> St.: This section includes the small drainage work of adding new storm drainpipe by saw cutting out the pavement, then restoring that pavement with new pavement. Other work includes grind and overlay, gravel, HMA thickened edge, driveway improvements, speed cushions, and channelization.

Schedule B work will include overlay, sidewalk, curb ramps, a new crossing, and an RRFB signal relocation at S 144<sup>th</sup> Street and 46<sup>th</sup> Ave S near Foster High School, which is identified on the NTCP Top-10 priority list. If Council chooses to move forward with Schedule B, it can be funded using NTCP CIP funding or remaining 104 fund balance.

# INFORMATIONAL MEMO Page 2

#### FINANCIAL IMPACT AND BID SUMMARY (All amounts include sales tax)

The Tucci & Sons bid for Schedule A and Schedule B combined, without continency is \$1,612,609.75. The funding for this project will be broken down into four funding sources since the work is relevant to multiple projects; and therefore, would utilize multiple budgets - Overlay & Repair, Neighborhood Traffic Calming Program (NTCP), the Small Drainage Program, which would use Surface Water Enterprise Funds, and the Complete Streets grant.

	<b>Bid Results Estimate</b>	Engineer's Estimate	Funding Source	2022 Budget
Schedule A	\$1,422,751.25	\$1,438,725.00	Overlay CIP	\$1,050,000.00
Schedule B	189,858.50	239,257.50	Fund Balance/NTCP CIP	250,000.00
Contingency (8%)	129,008.78		Complete Streets Grant	400,000.00
			Small Drainage CIP	85,000.00
Total	\$1,741,618.53	\$1,677,982.50	Total	\$1,785,000.00

#### **RECOMMENDATION**

Council is being asked to award construction of the 2022 Overlay and Repair Program to Tucci & Sons for both Schedule A and Schedule B in the amount of \$1,612,609.75, and to consider this item on the Consent Agenda of the June 27, 2022, Special Council Meeting.

ATTACHMENTS: 2022 CIP Page 2, 12 & 78

Vicinity Map
Bid Tabulation
Bid Award Letter

#### CITY OF TUKWILA CAPITAL PROJECT SUMMARY

2021 2026 to

**PROJECT: Traffic Calming/Residential Safety Improvements** Project No. 80010301

Programmatic approach to addressing neighborhood traffic concerns through a variety of methods. **DESCRIPTION:** 

Residential street improvements with sidewalks, safety improvements, and bike facilities.

JUSTIFICATION: Neighborhood revitalization by improving residential streets.


Future candidates are listed in the citywide comprehensive update and safety-based prioritization of STATUS:

residential street improvements, sidewalks, and bike lanes.

**MAINT. IMPACT:** Varies, depends on treatment(s) used.

Residential improvements and traffic calming features to reduce speeds and improve pedestrian and bicycl **COMMENT:** such as the speed cushions, RRFB crossings, LED enhanced signs, Radar driver feedback signs, etc.

FINANCIAL	Through	Estimated							
(in \$000's)	2019	2020	2021	2022	2023	2024	2025	2026	BEYOND
EXPENSES									
Design	63	50	100	100					
Land (R/W)									
Const. Mgmt.	37								
Construction	148	0		300					
TOTAL EXPENSES	248	50	100	400	0	0	0	0	0
FUND SOURCES									
ARPA Funding			100	400					
Awarded Grant									
Proposed Grant									
Mitigation Actual									
Mitigation Expected									
City Oper. Revenue	248	50	0	0	0	0	0	0	0
TOTAL SOURCES	248	50	0	0	0	0	0	0	0

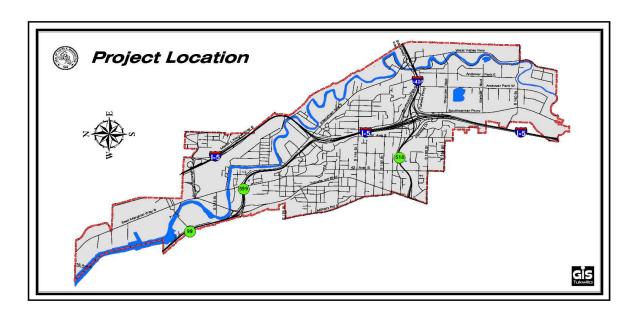

#### **CITY OF TUKWILA CAPITAL PROJECT SUMMARY**

2021 to 2026

PROJECT: Annual Overlay and Repair Program Project No. 9xx10401

**DESCRIPTION:** Select, design and construct asphalt and concrete pavement overlays of arterial and residential streets.

Preserve and maintain the street structure in a safe and useable state by resurfacing before failure which

JUSTIFICATION: also

minimizes costs. Some individual sites may be coordinated with water, sewer, and surface water projects.


Each year various sections of roadway throughout the City are designed and constructed for asphalt

STATUS: overlay.

MAINT. IMPACT: Reduces annual maintenance.

**COMMENT:** Ongoing project. Only one year actuals shown in first column.

FINANCIAL	Through	Estimated								
(in \$000's)	2019	2020	2021	2022	2023	2024	2025	2026	BEYOND	TOTAL
EXPENSES										
Design	209	190	150	150	150	150	150	150	150	1,449
Land (R/W)										0
Const. Mgmt.	121	15	200	200	200	200	200	200	200	1,536
Construction	1,224	312	1,050	1,050	1,050	1,050	1,150	1,150	1,300	9,336
TOTAL EXPENSES	1,554	517	1,400	1,400	1,400	1,400	1,500	1,500	1,650	12,321
FUND SOURCES										
Awarded Grant										0
Proposed Grant										0
Mitigation Actual										0
Mitigation Expected										0
City Oper. Revenue	1,554	517	1,400	1,400	1,400	1,400	1,500	1,500	1,650	12,321
TOTAL SOURCES	1,554	517	1,400	1,400	1,400	1,400	1,500	1,500	1,650	12,321

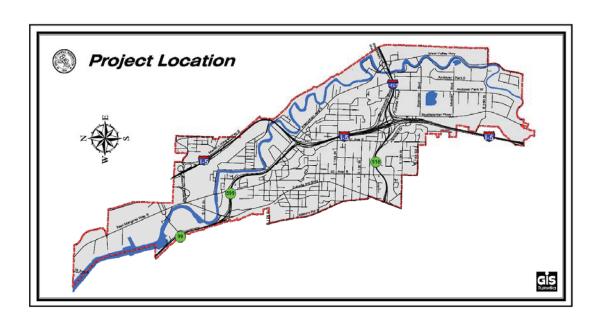

#### **CITY OF TUKWILA CAPITAL PROJECT SUMMARY**

2021 to 2026

PROJECT: Annual Small Drainage Program Project No. 9xx41201 81241207

**DESCRIPTION:** Select, design, and construct small drainage projects throughout the City.

JUSTIFICATION: Provide drainage corrections for existing/ongoing drainage problems throughout the City, including culvert

replacements, drain extensions, and pavement upgrades.


STATUS: Projects for this annual program are taken from Small Drainage Project List.


**MAINT. IMPACT:** Reduces maintenance.

COMMENT: Ongoing project, only one year shown in first column. Construction expenses may occur over two calendar

years.

FINANCIAL	Through	Estimated								
(in \$000's)	2019	2020	2021	2022	2023	2024	2025	2026	BEYOND	TOTAL
EXPENSES										
Design	74	92	100	100	100	100	110	110	80	866
Const. Mgmt.	40	68	100	100	100	100	110	110	80	808
Construction	108	515	700	700	700	700	750	750	513	5,436
TOTAL EXPENSES	222	675	900	900	900	900	970	970	673	7,110
FUND SOURCES										
Awarded Grant										0
Proposed Grant	65									65
Mitigation Actual										0
Mitigation Expected										0
Utility Revenue	157	675	900	900	900	900	970	970	673	7,045
TOTAL SOURCES	222	675	900	900	900	900	970	970	673	7,110

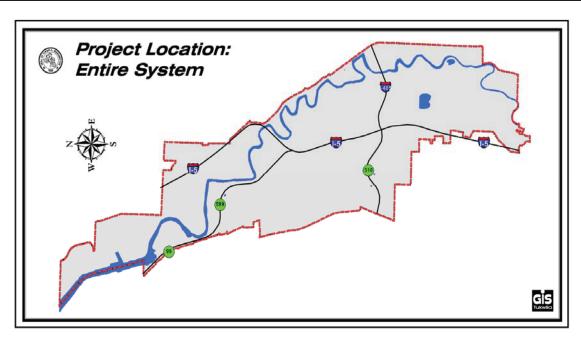

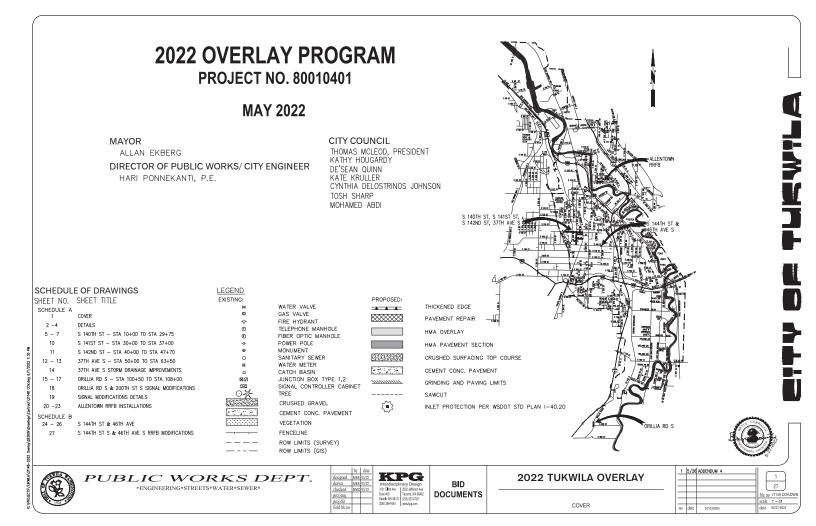

	TUKWILA /2022	- DEPARTMENT OF PUBLIC WORKS BID TAB - 2022 Overlay Program [Project No. 80010401]			Total		ADDAREN	T LOW BIDDER						
0,9						s Estimate		& SONS INC	MILES RE	SOURCES LLC	IC	ON	LAKESIDE IND	USTRIES INC
No.	Section No.	item	Quantity	Unit	Unit Cost	Total Cost	Unit Cost	Total Cost	Unit Cost	Total Cost	Unit Cost	Total Cost	Unit Cost	Total Cost
	AY IMPRO	RLAY & SIDEWALK IMPROVEMENTS DVEMENTS												
A1 A2	1-04 1-07	SPCC Plan	1	FA LS	\$ 2,250.00 \$	8,000.00 2,250.00	\$ 8,000.00 \$ 250.00	\$ 8,000.00 \$ 250.00	\$ 8,000.00 \$ 287.00	\$ 8,000.00 \$ 287.00	\$ 8,000.00 \$ 125.00	\$ 8,000.00 \$ 125.00	\$ 8,000.00 \$ 1,000.00	\$ 8,000.00 \$ 1,000.00
A3 A4 A5	1-09 1-10 1-10	Project Temporary Traffic Control	1 1 300	LS :		107,000.00 113,000.00 36,000.00	\$ 127,300.00 \$ 135,000.00 \$ 110.00	\$ 127,300.00 \$ 135,000.00 \$ 33,000.00	\$ 88,105.00 \$ 134,801.00 \$ 133.40	\$ 88,105.00 \$ 134,801.00 \$ 40,020.00	\$ 150,000.00 \$ 187,000.00 \$ 190.00	\$ 150,000.00 \$ 187,000.00 \$ 57,000.00	\$ 160,000.00 \$ 200,000.00 \$ 150.00	\$ 160,000.00 \$ 200,000.00 \$ 45,000.00
A5 A6 A7	2-02 2-02	Asphalt Pavement Removal	500 1	SY :	\$ 45.00 \$	22,500.00 8.500.00	\$ 10.00 \$ 10.00 \$ 40.000.00	\$ 33,000.00 \$ 5,000.00 \$ 40,000.00	\$ 133.40 \$ 33.10 \$ 2.560.00	\$ 40,020.00 \$ 16,550.00 \$ 2,560.00	\$ 190.00 \$ 78.00 \$ 12.500.00	\$ 57,000.00 \$ 39,000.00 \$ 12,500.00	\$ 150.00 \$ 75.00 \$ 7.500.00	\$ 45,000.00 \$ 37,500.00 \$ 7.500.00
A8 A9	2-02	Roadway Excavation Incl. Haul	1 40	LS CY :		20,000.00 3,800.00	\$ 60,000.00 \$ 100.00	\$ 60,000.00 \$ 4,000.00	\$ 62,360.00 \$ 98.25	\$ 62,360.00 \$ 3,930.00	\$ 25,500.00 \$ 190.00	\$ 25,500.00 \$ 7,600.00	\$ 17,500.00 \$ 50.00	\$ 17,500.00 \$ 2,000.00
A10 A11	2-03 4-04	Gravel Borrow Incl. Haul	200 650	TON :	\$ 25.00 \$ \$ 75.00 \$	5,000.00 48,750.00	\$ 35.00 \$ 60.00	\$ 7,000.00 \$ 39,000.00	\$ 100.30 \$ 87.05	\$ 20,060.00 \$ 56,582.50	\$ 64.00 \$ 85.00	\$ 12,800.00 \$ 55,250.00	\$ 30.00 \$ 60.00	\$ 6,000.00 \$ 39,000.00
A12 A13	5-04 5-04	HMA Cl. 1/2" PG 58H-22	60 2,850	TON :	\$ 125.00 \$ \$ 110.00 \$	7,500.00 313,500.00	\$ 375.00 \$ 115.00	\$ 22,500.00 \$ 327,750.00	\$ 529.00 \$ 142.00	\$ 31,740.00 \$ 404,700.00	\$ 350.00 \$ 122.00	\$ 21,000.00 \$ 347,700.00	\$ 350.00 \$ 130.00	\$ 21,000.00 \$ 370,500.00
A14 A15	5-04 5-04	Temporary Pavement	90	TON :	\$ 175.00 \$	15,750.00 5,250.00	\$ 250.00 \$ 150.00	\$ 22,500.00 \$ 4,500.00	\$ 370.35 \$ 155.50	\$ 33,331.50 \$ 4,665.00	\$ 260.00 \$ 200.00	\$ 23,400.00	\$ 240.00	\$ 21,600.00 \$ 6,000.00
A16 A17 A18	5-04 5-04	Thickened Edge Planing Bituminous Pavement Asphalt Cost Price Adjustment	1,110 16,150	SY :	\$ 8.00 \$ \$ 5.00 \$ \$ 10,000.00 \$	8,880.00 80,750.00 10,000.00	\$ 2.50 \$ 5.00 \$ 10,000.00	\$ 2,775.00 \$ 80,750.00 \$ 10,000.00	\$ 3.30 \$ 7.00 \$ 10,000.00	\$ 3,663.00 \$ 113,050.00 \$ 10,000.00	\$ 5.00 \$ 7.00 \$ 10,000.00	\$ 5,550.00 \$ 113,050.00 \$ 10,000.00	\$ 2.50 \$ 6.30 \$ 10,000.00	\$ 2,775.00 \$ 101,745.00 \$ 10,000.00
A19 A20	7-05 7-05	Adjust Manhole	7 32	EA EA	\$ 1,500.00 \$ \$ 1,100.00 \$	10,500.00 35,200.00	\$ 850.00 \$ 1,000.00	\$ 5,950.00 \$ 32,000.00	\$ 1,160.00 \$ 1,160.00	\$ 8,120.00 \$ 37,120.00	\$ 750.00 \$ 750.00	\$ 5,250.00 \$ 24,000.00	\$ 750.00 \$ 1,100.00	\$ 5,250.00 \$ 35,200.00
A21 A22	7-12 7-15	Adjust Water Valve	19 1	EA :	\$ 800.00 \$ \$ 3,500.00 \$	15,200.00 3,500.00	\$ 850.00 \$ 10,000.00	\$ 16,150.00 \$ 10,000.00	\$ 812.00 \$ 15,650.00	\$ 15,428.00 \$ 15,650.00	\$ 532.00 \$ 36,000.00	\$ 10,108.00 \$ 36,000.00	\$ 475.00 \$ 10,000.00	\$ 9,025.00 \$ 10,000.00
A23 A24	8-01 8-13		64 3	EA :	\$ 80.00 \$ \$ 700.00 \$	5,120.00 2,100.00	\$ 55.00 \$ 850.00	\$ 3,520.00 \$ 2,550.00	\$ 107.50 \$ 464.00	\$ 6,880.00 \$ 1,392.00	\$ 60.00 \$ 600.00	\$ 3,840.00 \$ 1,800.00	\$ 100.00 \$ 475.00	\$ 6,400.00 \$ 1,425.00
A25	1-05	ADA Features Surveying	1	LS		7,000.00	\$ 12,000.00	\$ 12,000.00	\$ 6,531.00	\$ 6,531.00	\$ 2,500.00	\$ 2,500.00	\$ 2,000.00	\$ 2,000.00
A26 A27	2-02	Cement Conc. Curb Removal Incl. Haul	250 780	LF :	\$ 60.00 \$	15,000.00 23,400.00	\$ 15.00 \$ 12.00	\$ 3,750.00 \$ 9,360.00	\$ 50.90 \$ 18.30	\$ 12,725.00 \$ 14,274.00	\$ 100.00 \$ 30.00	\$ 25,000.00 \$ 23,400.00	\$ 82.00 \$ 120.00	\$ 20,500.00 \$ 93,600.00
A28 A29 A30	7-05 8-04 8-06	Cement Conc. Curb and Gutter	1,700 180	LF SY	\$ 1,200.00 \$ \$ 50.00 \$ \$ 80.00 \$	1,200.00 85,000.00 14,400.00	\$ 1,000.00 \$ 40.00 \$ 90.00	\$ 1,000.00 \$ 68,000.00 \$ 16,200.00	\$ 1,015.00 \$ 33.75 \$ 62.65	\$ 1,015.00 \$ 57,375.00 \$ 11,277.00	\$ 500.00 \$ 32.50 \$ 100.00	\$ 500.00 \$ 55,250.00 \$ 18,000.00	\$ 1,000.00 \$ 33.00 \$ 100.00	\$ 1,000.00 \$ 56,100.00 \$ 18,000.00
A31 A32	8-06 8-14		35 500	SY :	\$ 80.00 \$ \$ 75.00 \$	2,800.00 37,500.00	\$ 90.00 \$ 70.00	\$ 3,150.00 \$ 35,000.00	\$ 62.65 \$ 53.00	\$ 2,192.75 \$ 26,500.00	\$ 100.00 \$ 81.25	\$ 3,500.00 \$ 40,625.00	\$ 100.00 \$ 80.00	\$ 3,500.00 \$ 40,000.00
A33 A34	8-14 8-14	Cement Conc. Curb Ramp Cement Conc. Pedestrian Curb	12 65	EA LF	\$ 4,000.00 \$	48,000.00 2,275.00	\$ 4,500.00 \$ 40.00	\$ 54,000.00 \$ 2,600.00	\$ 2,587.00 \$ 38.60	\$ 31,044.00 \$ 2,509.00	\$ 3,125.00 \$ 44.00	\$ 37,500.00 \$ 2,860.00	\$ 3,200.00 \$ 45.00	\$ 38,400.00 \$ 2,925.00
A35	7-04		70	TON :	\$ 60.00 \$	4,200.00	\$ 50.00	\$ 3,500.00	\$ 40.00	\$ 2,800.00	\$ 106.00	\$ 7,420.00	\$ 150.00	\$ 10,500.00
A36 A37	7-05 7-04	Ductile Iron Storm Sewer Pipe 6 In. Diam.	70 35	TON :	\$ 150.00 \$ \$ 110.00 \$	10,500.00 3,850.00	\$ 115.00 \$ 110.00	\$ 8,050.00 \$ 3,850.00	\$ 255.00 \$ 119.20	\$ 17,850.00 \$ 4,172.00	\$ 200.00 \$ 275.00	\$ 14,000.00 \$ 9,625.00	\$ 250.00 \$ 175.00	\$ 17,500.00 \$ 6,125.00
A38 A39	7-04 7-05		108 34	EA :	\$ 110.00 \$ \$ 350.00 \$	11,880.00 11,900.00	\$ 145.00 \$ 25.00	\$ 15,660.00 \$ 850.00	\$ 159.50 \$ 25.20	\$ 17,226.00 \$ 856.80	\$ 291.00 \$ 26.00	\$ 31,428.00 \$ 884.00	\$ 190.00 \$ 25.00	\$ 20,520.00 \$ 850.00
A40 A41 A42	7-05 7-05		3 2	EA EA	\$ 1,000.00 \$ \$ 3,000.00 \$ \$ 750.00 \$	1,000.00 9,000.00 1,500.00	\$ 1,200.00 \$ 2,000.00 \$ 1,500.00	\$ 1,200.00 \$ 6,000.00 \$ 3,000.00	\$ 1,787.00 \$ 2,223.00 \$ 1.725.00	\$ 1,787.00 \$ 6,669.00 \$ 3,450.00	\$ 4,150.00 \$ 3,100.00 \$ 3,700.00	\$ 4,150.00 \$ 9,300.00 \$ 7,400.00	\$ 4,200.00 \$ 2,500.00 \$ 3,500.00	\$ 4,200.00 \$ 7,500.00 \$ 7,000.00
A43 A44	8-31 8-32	Protect Utility Pole Resolution of Utility Conflicts	1 1	LS FA	\$ 2,500.00 \$	2,500.00 8.000.00	\$ 2,500.00 \$ 8,000.00	\$ 2,500.00 \$ 8,000.00	\$ 2,900.00 \$ 8,000.00	\$ 2,900.00 \$ 8,000.00	\$ 6,250.00 \$ 8,000.00	\$ 6,250.00 \$ 8,000.00	\$ 3,000.00 \$ 8,000.00	\$ 3,000.00 \$ 8,000.00
A45	8-32		3	EA		1,800.00	\$ 1,000.00	\$ 3,000.00	\$ 870.00	\$ 2,610.00	\$ 625.00	\$ 1,875.00	\$ 1,000.00	\$ 3,000.00
A46	8-20	Traffic Signal Modifications (Orillia Rd S & S 200th St), Complete	١,	LS	\$ 77.000.00 S	77.000.00	\$ 55,000.00	\$ 55,000.00	\$ 44.080.00	\$ 44.080.00	\$ 45,600.00	\$ 45.600.00	\$ 40,000,00	\$ 40,000.00
A47	8-20	RRFB Systen=m Installations ( S124th Street & 44th Avenue S and S 124th Street & 46th Avenue S), Complete	1	LS	\$ 75,000.00 \$	75,000.00	\$ 45,000.00	\$ 45,000.00	\$ 37,120.00	\$ 37,120.00	\$ 38,400.00	\$ 38,400.00	\$ 35,000.00	\$ 35,000.00
FRANCHI A48	SE UTILIT 8-19	TY ITEMS	1 1	EA :		900.00	\$ 2,000.00	\$ 2,000.00	\$ 2,900.00	\$ 2,900.00	\$ 1,875.00	\$ 1,875.00	\$ 2,000.00	\$ 2,000.00
A49	8-19	Adjust Gas Valve  OPMENT	5	EA :	\$ 700.00 \$	3,500.00	\$ 850.00	\$ 4,250.00	\$ 812.00	\$ 4,060.00	\$ 532.00	\$ 2,660.00	\$ 750.00	\$ 3,750.00
A50 A51		Erosion/Water Pollution Control	1 1	FA FA		4,250.00 7,000.00	\$ 4,250.00 \$ 7,000.00	\$ 4,250.00 \$ 7,000.00	\$ 4,250.00 \$ 7,000.00	\$ 4,250.00 \$ 7,000.00	\$ 4,250.00 \$ 7,000.00	\$ 4,250.00 \$ 7,000.00	\$ 4,250.00 \$ 7,000.00	\$ 4,250.00 \$ 7,000.00
A52	8-18		1	EA		2,500.00	\$ 400.00	\$ 400.00	\$ 870.00	\$ 870.00	\$ 740.00	\$ 740.00	\$ 2,000.00	\$ 2,000.00
A53 A54	8-05 8-21		8 1	EA LS		20,000.00 8,250.00	\$ 275.00 \$ 18,100.00	\$ 2,200.00 \$ 18,100.00	\$ 275.00 \$ 16,590.00	\$ 2,200.00 \$ 16,590.00	\$ 285.00 \$ 19,500.00	\$ 2,280.00 \$ 19,500.00	\$ 250.00 \$ 16,000.00	\$ 2,000.00 \$ 16,000.00
A55 A56	8-22 8-22		8 300	EA :	\$ 80.00 \$ \$ 50.00 \$	640.00 15,000.00	\$ 95.00 \$ 8.25	\$ 760.00 \$ 2,475.00	\$ 90.50 \$ 8.12	\$ 724.00 \$ 2,436.00	\$ 94.00 \$ 8.40	\$ 752.00 \$ 2,520.00	\$ 85.00 \$ 8.00	\$ 680.00 \$ 2,400.00
A57 A58	8-22 8-22		1,200 3,160	SF :	\$ 8.00 \$ \$ 3.00 \$ \$ 1.50 \$	9,600.00 9,480.00	\$ 7.25 \$ 0.85	\$ 8,700.00 \$ 2,686.00	\$ 7.25 \$ 0.85	\$ 8,700.00 \$ 2,686.00	\$ 7.50 \$ 0.85	\$ 9,000.00 \$ 2,686.00	\$ 7.00 \$ 0.90	\$ 8,400.00 \$ 2,844.00
A59 A60 A61	8-22 8-22 8-23	Paint Line, 4 Inch Plastic Yield Line Symbol Temporary Pavement Markings	7,800 17 4,600	EA :	\$ 1.50 \$ \$ 50.00 \$ \$ 0.50 \$	11,700.00 850.00 2,300.00	\$ 0.70 \$ 23.25 \$ 0.85	\$ 5,460.00 \$ 395.25 \$ 3,910.00	\$ 0.67 \$ 23.20 \$ 0.38	\$ 5,226.00 \$ 394.40 \$ 1,748.00	\$ 0.70 \$ 24.00 \$ 0.39	\$ 5,460.00 \$ 408.00 \$ 1,794.00	\$ 0.70 \$ 25.00 \$ 1.30	\$ 5,460.00 \$ 425.00 \$ 5,980.00
					RUCTION COST \$	1,438,725.00		\$ 1,422,751.25	7 0.30	\$ 1,493,742.95	J 0.33	\$ 1,616,865.00	7 1.30	\$ 1,626,829.00
ROADWA B1	1-04	OVEMENTS Unexpected Site Changes	1	FA	\$ 1,000.00 S	1.000.00	\$ 1,000.00	S 1.000.00	\$ 1.000.00	\$ 1.000.00	S 1.000.00	\$ 1.000.00	\$ 1.000.00	\$ 1,000.00
B2 B3	1-07 1-09	SPCC Plan	1	LS :	\$ 500.00 \$ \$ 25,000.00 \$	500.00 25,000.00	\$ 250.00 \$ 16,000.00	\$ 250.00 \$ 16,000.00	\$ 287.00 \$ 4,170.00	\$ 287.00 \$ 4,170.00	\$ 125.00 \$ 38,000.00	\$ 125.00 \$ 38,000.00	\$ 1,000.00 \$ 32,000.00	\$ 1,000.00 \$ 32,000.00
B4 B5	1-10 2-02		1 480	LS SY		30,000.00 21,600.00	\$ 22,000.00 \$ 10.00	\$ 22,000.00 \$ 4,800.00	\$ 44,465.00 \$ 8.25	\$ 44,465.00 \$ 3,960.00	\$ 62,000.00 \$ 70.00	\$ 62,000.00 \$ 33,600.00	\$ 60,000.00 \$ 65.00	\$ 60,000.00 \$ 31,200.00
B6 B7	2-02 2-02	Removal of Structure and Obstruction Roadway Excavation Incl. Haul	1	LS	\$ 1,000.00 \$ \$ 4,500.00 \$	1,000.00 4,500.00	\$ 8,000.00 \$ 7,000.00	\$ 8,000.00 \$ 7,000.00	\$ 3,538.00 \$ 7,885.00	\$ 3,538.00 \$ 7,885.00	\$ 12,300.00 \$ 10,000.00	\$ 12,300.00 \$ 10,000.00	\$ 7,000.00 \$ 35,000.00	\$ 7,000.00 \$ 35,000.00
B8 B9	2-03 2-03		10 100	CY :	\$ 95.00 \$ \$ 25.00 \$	950.00 2,500.00	\$ 100.00 \$ 35.00	\$ 1,000.00 \$ 3,500.00	\$ 119.20 \$ 94.60	\$ 1,192.00 \$ 9,460.00	\$ 190.00 \$ 90.00	\$ 1,900.00 \$ 9,000.00	\$ 50.00 \$ 30.00	\$ 500.00 \$ 3,000.00
B10 B11	4-04 5-04	Crushed Surfacing Top Course HMA Cl. 1/2" PG 58H-22	100 30	TON :	\$ 75.00 \$ \$ 110.00 \$	7,500.00 3,300.00	\$ 60.00 \$ 250.00	\$ 6,000.00 \$ 7,500.00	\$ 157.50 \$ 316.40	\$ 15,750.00 \$ 9,492.00	\$ 85.00 \$ 246.00	\$ 8,500.00 \$ 7,380.00	\$ 100.00 \$ 390.00	\$ 10,000.00 \$ 11,700.00
B12 B13	5-04 7-05		10 3	TON :		1,750.00 3,300.00	\$ 150.00 \$ 1,000.00	\$ 1,500.00 \$ 3,000.00	\$ 303.00 \$ 1,160.00	\$ 3,030.00 \$ 3,480.00	\$ 200.00 \$ 750.00	\$ 2,000.00 \$ 2,250.00	\$ 250.00 \$ 1,100.00	\$ 2,500.00 \$ 3,300.00
B14 B15		Adjust Water Valve Inlet Protection	1 5	EA :	\$ 800.00 \$ \$ 80.00 \$	800.00 400.00	\$ 850.00 \$ 55.00	\$ 850.00 \$ 275.00	\$ 812.00 \$ 99.85	\$ 812.00 \$ 499.25	\$ 532.00 \$ 60.00	\$ 532.00 \$ 300.00	\$ 475.00 \$ 100.00	\$ 475.00 \$ 500.00
B16	1-05		1	LS		3,500.00	\$ 3,000.00	\$ 3,000.00	\$ 3,271.00	\$ 3,271.00	\$ 2,382.00	\$ 2,382.00	\$ 2,500.00	\$ 2,500.00
B17 B18	2-02	Cement Conc. Curb Removal Incl. Haul	60 370 410	LF :	\$ 60.00 \$ \$ 30.00 \$	3,600.00 11,100.00	\$ 15.00 \$ 12.00 \$ 52.75	\$ 900.00 \$ 4,440.00	\$ 68.65 \$ 29.30	\$ 4,119.00 \$ 10,841.00	\$ 156.00 \$ 30.00	\$ 9,360.00 \$ 11,100.00	\$ 82.00 \$ 120.00	\$ 4,920.00 \$ 44,400.00
B19 B20 B21	8-04 8-06 8-14	Cement Conc. Driveway Entrance	410 40 80	SY S	\$ 50.00 \$ \$ 80.00 \$ \$ 75.00 \$	20,500.00 3,200.00 6.000.00	\$ 52.75 \$ 90.00 \$ 70.00	\$ 21,627.50 \$ 3,600.00 \$ 5,600.00	\$ 41.00 \$ 62.65 \$ 62.00	\$ 16,810.00 \$ 2,506.00 \$ 4,960.00	\$ 42.00 \$ 93.00 \$ 81.00	\$ 17,220.00 \$ 3,720.00 \$ 6,480.00	\$ 44.00 \$ 100.00 \$ 80.00	\$ 18,040.00 \$ 4,000.00 \$ 6,400.00
B22 B23	8-14 8-14	Cement Conc. Curb Ramp	3 100	EA LF	\$ 4,000.00 \$	12,000.00 3,500.00	\$ 2,500.00 \$ 40.00	\$ 7,500.00 \$ 4,000.00	\$ 2,025.00 \$ 38.60	\$ 4,960.00 \$ 6,075.00 \$ 3,860.00	\$ 3,125.00 \$ 43.75	\$ 9,375.00 \$ 4,375.00	\$ 3,200.00 \$ 45.00	\$ 9,600.00 \$ 4,500.00
DRAINAG B24	7-04		10	LF	\$ 110.00 \$	1,100.00	\$ 110.50	\$ 1,105.00	\$ 541.00	\$ 5,410.00	\$ 625.00	\$ 6,250.00	\$ 625.22	\$ 6,252.20
B25 B26	7-05 7-05	Catch Basin Type 2 48 In. Diam. Replace Existing Frame and Grate with Solid Locking Cover	1	EA EA	\$ 4,500.00 \$ \$ 1,200.00 \$	4,500.00 1,200.00	\$ 5,000.00 \$ 1,000.00	\$ 5,000.00 \$ 1,000.00	\$ 5,950.00 \$ 1,015.00	\$ 5,950.00 \$ 1,015.00	\$ 9,550.00 \$ 500.00	\$ 9,550.00 \$ 500.00	\$ 12,000.00 \$ 1,000.00	\$ 12,000.00 \$ 1,000.00
B27 B28	7-05 7-05	Storm Drain Marker	5	EA :	\$ 3,000.00 \$ \$ 500.00 \$	3,000.00 2,500.00	\$ 2,000.00 \$ 25.00	\$ 2,000.00 \$ 125.00	\$ 2,240.00 \$ 25.20	\$ 2,240.00 \$ 126.00	\$ 3,750.00 \$ 26.00	\$ 3,750.00 \$ 130.00	\$ 3,000.00 \$ 25.00	\$ 3,000.00 \$ 125.00
B29 B30	8-32 8-32 SIGNALS	Pothole Utility	1	EST		3,000.00 5,000.00	\$ 3,000.00 \$ 5,000.00	\$ 3,000.00 \$ 5,000.00	\$ 3,000.00 \$ 5,000.00	\$ 3,000.00 \$ 5,000.00	\$ 3,000.00 \$ 5,000.00	\$ 3,000.00 \$ 5,000.00	\$ 3,000.00 \$ 5,000.00	\$ 3,000.00 \$ 5,000.00
	8-20	RRFB Modifications (S 144th St & 46th Ave S), Complete	1	LS	\$ 20,000.00 \$	20,000.00	\$ 18,000.00	\$ 18,000.00	\$ 15,080.00	\$ 15,080.00	\$ 15,600.00	\$ 15,600.00	\$ 16,000.00	\$ 16,000.00
B32 B33	8-19		1	EA :		2,000.00 1,400.00	\$ 2,000.00 \$ 850.00	\$ 2,000.00 \$ 1,700.00	\$ 2,900.00 \$ 812.00	\$ 2,900.00 \$ 1,624.00	\$ 1,875.00 \$ 532.00	\$ 1,875.00 \$ 1,064.00	\$ 2,000.00 \$ 750.00	\$ 2,000.00 \$ 1,500.00
		OPMENT		FA :										
B34 B35 B36	8-01 8-02 8-18	Property Restoration	1 1	FA :	\$ 10,000.00 \$	4,250.00 10,000.00 2,500.00	\$ 4,250.00 \$ 10,000.00 \$ 400.00	\$ 4,250.00 \$ 10,000.00 \$ 400.00	\$ 4,250.00 \$ 10,000.00 \$ 870.00	\$ 4,250.00 \$ 10,000.00 \$ 870.00	\$ 4,250.00 \$ 10,000.00 \$ 740.00	\$ 4,250.00 \$ 10,000.00 \$ 740.00	\$ 4,250.00 \$ 10,000.00 \$ 2,000.00	\$ 4,250.00 \$ 10,000.00 \$ 2,000.00
	CONTRO	PL DEVICES  Raised Pavement Marker Type 1	25	EA		187.50	\$ 9.50	\$ 237.50	\$ 3.50	\$ 87.50	\$ 3.60	\$ 90.00	\$ 3.00	\$ 75.00
B38 B39	8-09 8-21	Raised Pavement Marker Type 2	150 1	EA :	\$ 5.00 \$ \$ 7,000.00 \$	750.00 7,000.00	\$ 3.50 \$ 350.00	\$ 525.00 \$ 350.00	\$ 9.30 \$ 1,200.00	\$ 1,395.00 \$ 1,200.00	\$ 9.60 \$ 375.00	\$ 1,440.00 \$ 375.00	\$ 8.00 \$ 350.00	\$ 1,200.00 \$ 350.00
B40 B41	8-22 8-22	Plastic Stop Line Plastic Crosswalk Line	30 200	LF :	\$ 50.00 \$ \$ 8.00 \$	1,500.00 1,600.00	\$ 8.25 \$ 7.25	\$ 247.50 \$ 1,450.00	\$ 8.10 \$ 7.25	\$ 243.00 \$ 1,450.00	\$ 8.40 \$ 7.50	\$ 252.00 \$ 1,500.00	\$ 8.00 \$ 8.00	\$ 240.00 \$ 1,600.00
B42	8-22	Paint Line, 4 Inch SCHEDULE B	180 ESTIMATED	LF :	\$ 1.50 \$	270.00 <b>239,257.50</b>	\$ 0.70	\$ 126.00 \$ 189,858.50	\$ 0.67	\$ 120.60 \$ 223,423.35	\$ 0.70	\$ 126.00 \$ 318,391.00	\$ 0.70	\$ 126.00 \$ 363,253.20
					B = TOTAL BID			\$ 1,612,609.75		\$ 1,717,166.30		\$ 1,935,256.00		\$ 1,990,082.20



June 8, 2022

Hari Ponnekanti, P.E. City of Tukwila 6200 Southcenter Boulevard Tukwila, WA 98188

RE: 2022 Overlay Program [Project No. 80010401]

Dear Mr. Ponnekanti,

As requested, KPG PSOMAS has completed the verification for Tucci & Sons, Inc. for the 2022 Overlay Program for their bid in the amount of \$1,612,609.75 (Schedule A plus Schedule B).

We have also checked the status of Tucci & Sons, Inc. on the Washington State Labor and Industries web page to confirm they are currently insured, bonded, and licensed. Additionally, no strikes or debarment records arose federally or statewide regarding Tucci & Sons, Inc.

Additionally, we called Tucci's references as listed in the bid documents. All calls were answered by machine and messages were left. Should we receive any responses we will forward that information on to you.

It is KPG PSOMAS' recommendation that the 2022 Overlay Program Schedule A bid work in the amount of \$1,422,471.25 be awarded to Tucci & Sons, Inc. The Schedule B bid work in the amount of \$189,858.50 will be awarded at the sole discretion of the City.


We have enclosed the contractor verification package for your review.

Sincerely, KPG PSOMAS

Bryce Corrigan, P.E.

Begre Conyw

Enclosures: Tucci & Sons, Inc - Verification Package



## **Contractors**

#### **TUCCI & SONS INC**

Owner or tradesperson TUCCI, MICHAEL F

Principals

TUCCI, MICHAEL F, PRESIDENT

TUCCI, TIMOTHY F, SECRETARY

TUCCI, JAMES G

(End: 01/01/1980)

XITCO, JOHN V

(End: 01/01/1980)

TUCCI, THOMAS D

(End: 01/01/1980)

Doing business as TUCCI & SONS INC

WA UBI No.

278 021 315

Business type

4224 WALLER RD TACOMA, WA 98443

253-922-6676

**PIERCE County** 

Corporation

#### License

Verify the contractor's active registration / license / certification (depending on trade) and any past violations.

**Construction Contractor** 

Active

Meets current requirements.

License specialties

**GENERAL** 

License no.
TUCCIS\*379N0

Effective — expiration

08/20/1963— 01/14/2024

Bond

**TRAVELERS CAS & SURETY CO** 

\$12,000.00

Bond account no.

081S103486221BCM

Received by L&I 12/27/2001 Effective date

01/01/2002

Expiration date

**Until Canceled** 

Insurance

**Zurich American Ins Co** 

\$1,000,000.00

Policy no.

GLO399266918

Received by L&I

12/22/2021

Effective date

01/01/2022

Expiration date

01/01/2023

Insurance history

Savings

No savings accounts during the previous 6 year period.

Lawsuits against the bond or savings

No lawsuits against the bond or savings accounts during the previous 6 year period.

L&I Tax debts

1/3

#### **TUCCI & SONS INC**

No L&I tax debts are recorded for this contractor license during the previous 6 year period, but some debts may be recorded by other agencies.

No license violations during the previous 6 year period.

#### Certifications & Endorsements

#### **OMWBE Certifications**

No active certifications exist for this business.

Apprentice Training Agent
Registered training agent. Check their eligible programs and occupations.

#### Workers' Comp

Do you know if the business has employees? If so, verify the business is up-to-date on workers' comp premiums.

This company has multiple workers' comp accounts.

#### **Active accounts**

L&I Account ID 700,260-00

This business is certified to cover its own workers' comp costs. No premiums due.

Doing business as **TUCCI & SONS INC** 

Estimated workers reported

N/A

L&I account contact

- Email: @Ini.wa.gov Track this contractor (2)

#### **Public Works Requirements**

Verify the contractor is eligible to perform work on public works projects.

Required Training- Effective July 1, 2019 Exempt from this requirement.

**Contractor Strikes** 

No strikes have been issued against this contractor.

Contractors not allowed to bid

No debarments have been issued against this contractor.

#### Workplace Safety & Health

Check for any past safety and health violations found on jobsites this business was responsible for.

Inspection results date

10/20/2021

No violations

Self Insured.

Inspection no. 317965712

Location

2623 south 170th st

Seatac, WA 98188

Inspection results date

08/28/2017

Inspection no. 317946151

Location

3205 MARTIN WAY E

Olympia, WA 98506

Inspection results date

09/28/2016

Inspection no.

317941904

No violations

No violations

Location W. Valley HWY S. & W. Main St Auburn, WA 98001



#### **Department of Labor & Industries**

## Certificate of Workers' Compensation Coverage

June 8, 2022

WA UBI No.	278 021 315			
L&I Account ID	700,260-00			
Legal Business Name	TUCCI & SONS INC			
Doing Business As	TUCCI & SONS INC			
Workers' Comp Premium Status:	Self Insured. This business is certified to cover its own workers' comp costs. No premiums due.			
Estimated Workers Reported (See Description Below)	N/A			
Account Representative	Employer Services Help Line, (360) 902-4817			
Licensed Contractor?	Yes			
License No.	TUCCIS*379N0			
License Expiration	01/14/2024			

# What does "Estimated Workers Reported" mean?

Estimated workers reported represents the number of full time position requiring at least 480 hours of work per calendar quarter. A single 480 hour position may be filled by one person, or several part time workers.

#### **Industrial Insurance Information**

Employers report and pay premiums each quarter based on hours of employee work already performed, and are liable for premiums found later to be due. Industrial insurance accounts have no policy periods, cancellation dates, limitations of coverage or waiver of subrogation (See RCW 51.12.050 and 51.16.190).



#### Susiness Lookup

**License Information:** 

New search Back to results

**Entity name:** 

TUCCI & SONS, INC.

**Business name:** 

TUCCI & SONS, INC.

**Entity type:** 

**Profit Corporation** 

UBI#:

278-021-315

**Business ID:** 

001

Location ID:

0004

Location:

Active

**Location address:** 

11102 S STEELE ST

TACOMA WA 98444

Mailing address:

4224 WALLER RD E

TACOMA WA 98443

Excise tax and reseller permit status:

Click here

**Secretary of State status:** 

Click here

#### **Endorsements**

Endorsements held at this loc License #	Count	Details	Status	Expiration dat First issuance
Scale - Large	2		Active	Mar-31-2023 Apr-18-2001

### Governing People May include governing people not registered with Secretary of State

**Governing people** 

Title

KEVER, KEVIN A

TUCCI, MICHAEL A

TUCCI, MICHAEL F

TUCCI, TIMOTHY F



#### **View Additional Locations**

The Business Lookup information is updated nightly. Search date and time: 6/8/2022 10:31:51 AM



#### **Contact us**

How are we doing?

Take our survey!

Don't see what you expected?

Check if your browser is supported





## TUCCI & SONS INC

Unique Entity ID

CAGE / NCAGE

Purpose of Registration

K5N5ZMTJJEM8

0HXL1

**All Awards** 

Registration Status Active Registration **Expiration Date** Jun 2, 2023

Physical Address

Mailing Address

4224 Waller RD E

4224 Waller RD E

Tacoma, Washington 98443-1623

Tacoma, Washington 98443-1623

**United States** 

**United States** 

Business Information

Doing Business as

**Division Name** 

**Division Number** 

(blank)

(blank)

(blank)

Congressional District Washington 10

State / Country of Incorporation Washington / United States

URL (blank)

**Registration Dates** 

**Activation Date** 

Submission Date

Initial Registration Date

Jun 6, 2022 Jun 2. 2022 Mar 18, 2002

**Entity Dates** 

**Entity Start Date** 

Fiscal Year End Close Date

Jan 1, 1950

Dec 31

**Immediate Owner** 

CAGE

Legal Business Name

(blank)

(blank)

**Highest Level Owner** 

CAGE

Legal Business Name

(blank)

(blank)

#### **Executive Compensation**

Registrants in the System for Award Management (SAM) respond to the Executive Compensation questions in accordance with Section 6202 of P.L. 110-252, amending the Federal Funding Accountability and Transparency Act (P.L. 109-282). This information is not displayed in SAM. It is sent to USAspending.gov for display in association with an eligible award. Maintaining an active registration in SAM demonstrates the registrant responded to the questions.

#### **Proceedings Questions**

Registrants in the System for Award Management (SAM) respond to proceedings questions in accordance with FAR 52.209-7, FAR 52.209-9, or 2.C.F.R. 200 Appendix XII. Their responses are not displayed in SAM. They are sent to FAPIIS.gov for display as applicable. Maintaining an active registration in SAM demonstrates the registrant responded to the proceedings questions.

#### xclusion Summary

Active Exclusions Records?

No

#### AM Search Authorization

I authorize my entity's non-sensitive information to be displayed in SAM public search results:

Yes

#### **Business Types**

**Entity Structure** 

**Entity Type** 

Organization Factors

Corporate Entity (Not Tax Exempt)

**Business or Organization** 

**Manufacturer of Goods** 

**Profit Structure** 

For Profit Organization

#### Socio-Economic Types

Check the registrant's Reps & Certs, if present, under FAR 52.212-3 or FAR 52.219-1 to determine if the entity is an SBA-certified HUBZone small business concern. Additional small business information may be found in the SBA's Dynamic Small Business Search if the entity completed the SBA supplemental pages during registration.

Financial Information	
Accepts Credit Card Payments No	Debt Subject To Offset  No
EFT Indicator	CAGE Code 0HXL1

#### oints of Contact

#### **Electronic Business**

4224 Waller RD E

**KEVIN A KEVER** 

Tacoma, Washington 98443

**United States** 

MICHAEL TUCCI

4224 Waller RD

Tacoma, Washington 98443

**United States** 

#### **Government Business**

4224 Waller RD E

**KEVIN A KEVER** 

Tacoma, Washington 98443

**United States** 

MICHAEL TUCCI

4224 Waller RD

Tacoma, Washington 98443

United States

#### Service Classifications

#### **NAICS Codes**

Primary Yes

**NAICS Codes** 

237310

Highway, Street, And Bridge Construction

**NAICS Title** 

237110

Water And Sewer Line And Related Structures Construction

324121

**Asphalt Paving Mixture And Block Manufacturing** 

#### Isaster Response

Yes, this entity appears in the disaster response registry.

Bonding Levels	Dollars
(blank)	(blank)

States

Counties

Washington

WA: Thurston, Pierce, King

Metropolitan Statistical Areas

(blank)

#### **Certified Firms Directory**

MWBE's Directory of Certified Firms will help buyers and contracting officers quickly locate and notify rms of upcoming procurement and contracting opportunities. When you search, you must also select at east one certification type.

nis online directory lists firms certified by OMWBE. Firms that appear in the directory are currently certified and approved to be utilized toward meeting established contract goal their displayed certification type(s). Firms that are noted as suspended cannot be utilized for-credit in new contracts until the suspension is removed. For additional details pleas ference the <u>US DOT regulations</u> or contact Amal Joury at <u>amalj@omwbe.wa.gov</u>.

As of October 1, 2020, the Washington State Department of Transportation (WSDOT) will be adding white-women owned businesses back into the Federal Highway Administration race-conscious, or goals portion of the Disadvantaged Business Enterprise (DBE) Program. All previously awarded contracts with underutilized DBE (UDBE) goals will remain the same. This means only UDBE firms will continue to count toward those projects. On projects with goals set after October 1, 2020, all DBE firms will count toward all DBE goals. For more information, please contact (360) 705.7090.

WSDOT continues to implement a Small Business Enterprise Program on federal aid-projects. For more information on how to use the Directory of Certified Firms to find certified Small Businesses, please visit: <a href="https://www.wsdot.wa.gov/sites/default/files/2016/05/10/OEO-FSBE-DMCS-Search-Instructions.pdf">https://www.wsdot.wa.gov/sites/default/files/2016/05/10/OEO-FSBE-DMCS-Search-Instructions.pdf</a>

Show directory information and instruction

# CERTIFICATIONS Disadvantaged Business Enterprise (DBE) Minority Business Enterprise (MBE) Minority/Women Business Enterprise (MWBE) Small Business Enterprise (SBE) Socially and Economically Disadvantaged Business Enterprise (SEDBE) Women Business Enterprise (WBE) BUSINESS NAME/DBA TUCCI & SONS, INC.

#### Search Results

O firms with O certifications found

Your search parameters did not return any matches. Click Edit Parameters, modify the information in the fields above and click Search Again.
